

Preventive maintenance IDEV

February, 09 2021, Annual visit



Customer Customer Ref. :

Customer Company :

Site contact name : Geir Vistung Site contact Tel :

Site contact email :

Site company : Digiplex Norway AS - Holtskogen

Site address : Holtskogen 31, 1825 Tomter

Site country : Norway Customer account :

Room name : Digiplex - Holtskogen POD B

Field Service Engineer Service Request # / Activity : / WO-08409897

FSE name : Mario dos Santos Service District : Secure power - Norway

FSE address : Sandstuveien 68

Visit results

Kompressor la ut på lavttrykks pressostet under oppstart pga lav utetemperatur, og startet kun ved tuning via Cooling Tuner. Mistenker noe lav totalfylling av kuldemedium. Kompressoren rakk ikke å stabilisere seg tilstrekkelig under drift grunnet lav last og utetemperatur. Maskinen fungerer ellers som forventet.

(FSE) Recommendations / required actions

Sjekk av totalfylling blir fulgt opp snarest, og avtales nærmere med kunden for utbedring.

Etter avtale med kunden er timeteller for Air filter service alarm og Unit service alarm deaktivert. Dette da filter sjekkes ved hver service. Se øvrige kommentarer i rapporten.

Signature

Customer signature Schneider Electric signature

Geir Vistung Mario dos Santos



Equipment data Customer Ref. :

Equipment concerned : IDEV Install/Startup date : September, 29 2020

Serial number : SCE153573 Capacity : 52.5 kW

Configuration : Group configuration

Unit number within group system: 2 / 2

Main Information	
Room & environmental conditions	Cooling
25.7 °C	12.00%
Ambient temperature	Room environment humidity
	Equipment age: 0 years, 4 months, 28 days

Visit data		Customer Ref. :	
Service Request # / Ac	tivity:/WO-08409897		
Work time start	: February, 09 2021 11:33	Work time end	: February, 09 2021 11:33
Entitlement#	:	Entitlement name	:
Account ID	:	ISX Solution	:

Part 2022 2023 2024 2025 2026 2027 2028 2029 2030 Air filter Compressor Fan Cards

Contactor

Synthesis page

hecks carried out	Status when leaving	Comments
System Room Check		
System check		
Visual Check	•	
Electric environment checking	•	
Electrical measurement	•	
Unit inspection		
Unit Functional check		Unit Functional check: Fuktindikator i seglasset indikerer at anlegget er tørt. Flashgass i seglasset under drift av kompressor kan indikere mangel på kuldemedium. Pga lav last i rommet og lav utetemperatur rekker kompressoren ikke stabilisere seg tilstrekkelig.
Heating check	•	
Serial Numbers	•	
Settings	•	
Service and Parts		
Parts with Life Duration	•	
IT Room Assessment		
Air flow check		
Final Check	•	
Notes		
Comments	•	

Did you know?



Circulation of cool air in a computer room is rarely optimized; typically only 30 to 50% of this air is actually employed to cool the IT equipments.

The ever increasing requirement for more density in today's IT equipment only heightens the need for data center air management specialists, who are properly trained to diagnose the computer room air flow and temperature requirements and recognize issues that can be corrected by implementing simple best practices. Improved management of airflow in your IT room can result in:

Lower Costs - Reduced energy consumption and cold air demands.

Increased Availability - Improved server cooling results in higher reliability.

Increased Capacity - Better cooling efficiency increases equipment performance and eliminates the need to add more cooling units.

Schneider Electric's commitment:

Schneider Electric is committed to helping customers reduce energy costs and carbon emissions by 30%.

Deploying new technologies such as blade servers and virtualization create new challenges in terms of power, cooling and energy management. In addition, the capacity requirements of many Data Centers has been multiplied by 30 in 2 years, all experts agree that this rise will continue to accelerate.

Optimizing the power consumption of computer rooms and data centers is critical and may require leveraging new technologies to achieve economies in power consumption. These economies are substantial.


To turn our words into action, our Schneider Electric's Field Service Engineers have received specific training to enable them to diagnose the effectiveness of the airflow in your IT rooms.

On the next page you will find the results of this evaluation.


For more information on optimizing energy usage and availability in your data center, call one of our Energy Specialists on **http://www.schneider-electric.com.** To learn more please view our short <u>video</u> "Energy Management Services for Your Data Center". You can also download free white papers on this subject at **www.apc.com/en** (under "Support" - "learn "-" White Papers ")


Cooling unit alignments To optimize a raised-floor cooling system, cooling units must be


aligned with hot aisles.




Cable cutouts in a raised floor environment should be sealed to avoid bypass airflow.









Prevent hot exhaust from re-entering the equipment's intake by installing blanking panels in all of the empty front panel U-spaces in the rack.



intake side by removing any openings (gaps) in the rows.





located above the hot aisle.


Maintenance summary

Sjekk av totalfylling blir fulgt opp snarest, og avtales nærmere med kunden for utbedring.

Etter avtale med kunden er timeteller for Air filter service alarm og Unit service alarm deaktivert. Dette da filter sjekkes ved hver

Se øvrige kommentarer i rapporten.

Installation configuration



Comments

Customer

No comment

Customer issues

Customer

No comment

Schneider Electric

No comment

List of measurement devices

Device type	Device model	Serial number	Last calibration date
Multimeter	179	25940502	12 December 2017
Refrigerant Leak Detector	D-TEK	To be filled	09 October 2017
Oscilloscope	Fluke 43B	28440409	10 September 2015
Thermometer	ETI	D19401199	05 November 2020

1 System Room Check

Room environment

The environment where the equipment is located is suitable	Yes	
for service operation.		
Specify the type of room where the unit is located.	Electrical Room	
Specify the type of cooling used in the room.		Satisfactory
Measure and record the room temperature:	25.7 °C	Satisfactory
Room Environment Humidity	12 %	Satisfactory
There is sufficient access to operate on the unit	Yes	

Customer Room Designation

Record the customer room designation: Digiplex - Holtskogen POD B Done

2 System check

2.1 Visual Check

Model number of the unit IDAV1511A

Inspection

Visual check for foreign conducting materials inside and on top equipment

Satisfactory

2.2 Electric environment checking

Cable wiring

Power input/output wiring and ground cables checked for	Yes
tightness	
Field installed communication wiring check for tightness	Yes

2.3 Electrical measurement

Main input power supply measurements - Single phase

L1-N	239 V
L1-Ground	239 V

Main input power supply measurements - Three phases

L1-L2	408 V
L2-L3	408 V
L3-L1	408 V
L1-Ground	235.5 V
L2-Ground	236 V
I 3-Ground	236 V

Transformer Voltage Check

Transformer 1 Primary	235.5 V
Transformer 1 Secondary 1	25.7 V
Transformer 1 Secondary 2	25.6 V
Transformer 2 Primary	0 V
Transformer 2 Secondary 1	0 V
Transformer 2 Secondary 2	0 V
Transformer 3 Primary	0 V
Transformer 3 Secondary 1	0 V

3 Unit inspection

3.1 Unit Functional check

The unit firmware has been upgraded.	No
Installed firmware version	Display: aos_656.bin/bootmon_108.bin/Ledx2g_e11_600.bin / Unit 1.2.4.002_DFC.bin
Field Service Bulletins have been performed	No
Fan Motors Current Measurements - Three phases	
Total current of fan motors 1, 2 and 3 : L1	7.5 A
Total current of fan motors 1, 2 and 3 : L2	7.6 A
Total current of fan motors 1, 2 and 3 : L3	7.5 A
Controller	
The controller and user interface addresses are configured properly	Yes
The user interface display is working properly	Yes
The controller is properly configured for the unit type and	Yes
options installed	
Air flow	
All blowers move freely with no noise	Yes
The fans achieve the desired speed setting and have the correct rotation	Yes
Fan speed (% of maximum)	75 %
External air dampers are open and working properly	Yes
The air flow differential pressure switch has been calibrated and tested	Yes
Air filter	
The air filters were replaced	No
The air filter run hours were reset to zero	No
The air filter differential pressure switch has been tested	Yes
Cooling	
All air bleed valve caps are installed and secure	Yes
Sensor	
All of the sensors are reading properly	Yes
Return air temperature	25.7 °C
Return air % relative humidity	13 %
Delivery air temperature	25.7 °C
Chilled water inlet temperature	0 °C
Hot water inlet temperature	0 °C
Chilled water outlet temperature	0 °C
	0 °C
Hot water outlet temperature	0 C
Hot water outlet temperature Circuit 1 check	
	Yes

Circuit 1 measurements

Suction pressure	8.5 bar
Superheat temperature	7.2 °C
Suction line temperature	12.8 °C
Discharge pressure	19.1 bar
Subcooling temperature	6.8 °C
Liquid line filter temperature gradient	0 °C
Condenser inlet liquid temperature	0 °C
Condenser outlet liquid temperature	0 °C
Compressor current 1, L1	19.6 A
Compressor current 1, L2	18.6 A
Compressor current 1, L3	19.4 A
Compressor current 2, L1	0 A
Compressor current 2, L2	0 A
Compressor current 2, L3	0 A

Circuit 2 check

Sight glass indicates the system is dry	Yes
Circuit responds to the cooling demand	Yes

Circuit 2 measurements

Suction pressure	0 bar
Suction line temperature	0 °C
Superheat temperature	0 °C
Discharge pressure	0 bar
Subcooling temperature	0°C
Liquid line filter temperature gradient	0 °C
Condenser inlet liquid temperature	0 °C
Condenser outlet liquid temperature	0°C
Compressor current 1, L1	0 A
Compressor current 1, L2	0 A
Compressor current 1, L3	0 A
Compressor current 2, L1	0 A
Compressor current 2, L2	0 A
Compressor current 2, L3	0 A

Section comments

Fuktindikator i seglasset indikerer at anlegget er tørt.

The electric heaters respond to the demand

Flashgass i seglasset under drift av kompressor kan indikere mangel på kuldemedium.

Pga lav last i rommet og lav utetemperatur rekker kompressoren ikke stabilisere seg tilstrekkelig.

3.2 Heating check

Total electric heat current, L1

Total electric heat current, L2

Total electric heat current, L3

Total electric heat current, L1	4.5 A	
Total electric heat current, L2	4.4 A	
Total electric heat current, L3	4.3 A	
Electric Heat Current Measurements Lev	el 2	
Electric Heat Current Measurements Lev	el 2 8.8 A	
	-	

13.3 A

13.3 A

12.8 A

Yes

3.3 Serial Numbers

Out Door Heat Exchanger - Three phases

Model number	OCC1701LTB		
Serial number	EB202000053		
Measurements			
L-N	4.8 A	235.5 V	
L1-L2	0 A	0 V	
L1-L3	0 A	0 V	
L2-L3	0 A	0 V	
L-Ground	0 A	0 V	

3.4 Settings

Group configuration

Cycle time	0 h	No	
Number of stand-by units	0		
Setpoints			
Cooling set point	26 °C		

Cooling set point	26 °C	
Cooling proportional band	0 °C	
Dehumidification set point	55 %	
Dehumidification proportional band	15 %	
Humidification set point	0 %	
Humidification proportional band	0 %	
Delivery air temperature set point	0 °C	

Alarm Thresholds

High room temperature	40 °C
Low room temperature	17.8 °C
High room humidity	80 %
Low room humidity	0 %
High delivery air temperature	28.8 °C

4 Service and Parts

4.1 Parts with Life Duration

4.1.1 Compressor

Reference

Quantity0JustificationOther

Installation date 29 September 2020

Next replacement date 2030

4.1.2 Air filter

Reference

Quantity 2
Justification Other

Installation date 29 September 2020

Next replacement date 2022

4.1.3 Fan

Reference

Quantity0JustificationOther

Installation date 29 September 2020

Next replacement date 2030

4.1.4 Cards

Reference

Quantity0JustificationOther

Installation date 29 September 2020

Next replacement date 2030

4.1.5 Contactor

Reference

Quantity0JustificationOther

Installation date 29 September 2020

Next replacement date 2030

5 Final Check

Final Inspection

The area around the Unit is clean and orderly	Yes
The unit is completely operational	No
Active alarms are present	No
The interior/exterior of the unit is clean and free of debris	Yes
Interior and exterior panels are securely fastened	Yes

6 Notes

6.1 Comments

General comments

No comment


Unit Functional check

Fuktindikator i seglasset indikerer at anlegget er tørt.
Flashgass i seglasset under drift av kompressor kan indikere mangel på kuldemedium.
Pga lav last i rommet og lav utetemperatur rekker kompressoren ikke stabilisere seg tilstrekkelig.

SERVICES SOLUTIONS FROM A TRUSTED ADVISOR

Rely on Schneider Electric Critical Power & Cooling Services to protect your UPS from unexpected issues and downtime. Trained and trusted professionals are at your disposal to support and provide high quality service for your equipments.

Life Cycle Services

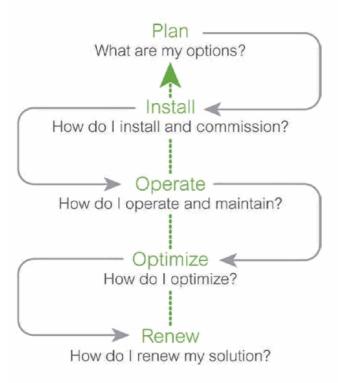

Schneider Electric Critical Power & Cooling Services (CPCS) provides the expertise, services, and support you need for your building, industry, power, or data center infrastructure.

- Experience: Our proud 170-year history has led us to worldwide recognition as the thought leader in energy management, power and cooling infrastructure, and energy efficiency.
- Reputation: Our highly trained teams technical support, project managers, Field Service Engineers (FSEs) — and our strong commitment to quality service have earned us a reputation as a trusted advisor in the industries we serve.
- Availability: Our extensive worldwide service network is one of the largest in the world. This enables us to deliver service where and when you need it.
- Expertise: Our highly skilled, certified FSEs are trained directly by the product developers themselves. This provides them with the highest level of system knowledge, resulting in accurate and quick diagnosis and repair.
- Speed: If equipment issues should arise, our technical support team is only a phone call away, ready to help you quickly diagnose the problem.
 When on-site help is required, our service plans dispatch a FSE rapidly, ensuring your system is up and running as fast as possible.

Plan

Assessment: Site survey, engineering analysis, environmental inspection.

Design Planning: Free online tools to plan and design tailor-made solutions.

Install

Project Management: Assistance in completing rollouts on time and within budget.

Installation: Equipment implementation and optimization, physical assembly and logistics coordination.

Start-up: Initial setup, installation, verification.

Training: Onsite equipment orientation, operational and maintenance education.

Operate

Service Plans: comprehensive onsite service packages with either Next-Business-Day availability or response upgrades to 4-hour and 8-hour.

Monitoring Service: 24*7 digital monitoring service with instant access to data and experts through Smartphone apps well as operational insights and analytics.

Preventive Maintenance: Corrective maintenance, system cleaning, environmental inspection, functional verification, and free firmware upgrades.

Optimize

Asset Capacity Trending: proactive asset planning guidance, along with analysis of critical power, cooling, and room layout domains.

Data Center Health Check: Site-level assessment as well as inventory list for Schneider Electric and 3rd party vendor equipment.

Renew

Modular Power Revitalization: comprehensive on-site UPS refresh service for modular UPS solutions, updated by certified service professionals.

Modernization Services: solutions to protect your aging UPS from unexpected issues and downtime. Assets' availability will increase and investments maximized.

For more information, please visit Critical Power & Cooling Services website at: http://www.schneider-electric.com/b2b/en/services/field-services/critical-power-and-cooling/
